CANDIDATE

AG-0009-KJN

TEST

1TE061 Industrial Project Management 17/3

Subject code	--
Evaluation type	--
Test opening time	17.03.2021 10:00
End time	17.03.2021 11:30
Grade deadline	--
PDF created	01.10.2023 02:14

1 Ny uppgift

Which of the following roles suits the "Reference group" in a given project ?
Select one alternative:

- lead project changes
- Forum for testing ideas ✔
- Conduct new assesments ✖
- Form alternative opinions

Wrong. 0 of 1 marks.

2 Ny uppgift

A project manager performs Earned Value Analysis and finds the following results: AC: 220,000, PV: 250,000, EV: 220,000.
Välj ett alternativ:

- CV = 1
- CV = 0. ✔
- CV = -30,000
- CV = 30,000.

Correct. 1 of 1 marks.

3 Ny uppgift

Which of the following description suits well Goal seeking projects
Select one alternative:

- Measurable goals set in advance
- A Well & Clear definied scope
- iterative process and agile project models ✓
- Enthusiasm, Hope, Panic, Solution.

Correct. 1 of 1 marks.

4 Ny uppgift

During human resource planning you identified that your team members are not sufficiently qualified for their tasks. Which of the following may be an appropriate solution to this problem?
Select one alternative:

- Increase employees monitoring
- Develop a training plan ✓
- Reduce the project scope/goal
- Develop intensive motivation plans for the staff

Correct. 1 of 1 marks.

5 Ny uppgift

Which of the following statements is not true?
Välj ett alternativ:

- Cultural differences will always be an obstacle to be overcome. ✔
- There is a common ground for people from different cultures on which they can interact without unsolvable conflicts
- Culture is a critical lever for competitive advantage. ✖
- Cultural differences are a resource to be fully utilized.

Wrong. 0 of 1 marks.

6 Ny uppgift

Which of the following is not part of the iron triangle
Select one alternative:

- Times
- Deliverables ✔
- Cost ✖
- Quality

Wrong. 0 of 1 marks.

7 Ny uppgift

Your organization is considering to run a project which will entail an investment of $1,000,000. The product from the project is forecasted to create revenues of $250,000 in the first year after the end of the project and of $420,000 in each of the two following years. What should the decision be?

Select one alternative:

- Revise the project cost
- Abandon the project
- Go ahead with the project ✓
- Create a new pre-study

Correct. 1 of 1 marks.

8 Ny uppgift

In the purchasing process, which of the following is the output of Source Selection?

Select one alternative:

- Proposals.
- Evaluation criteria
- Contract ✓
- Contract negotiation

Correct. 1 of 1 marks.

9 Ny uppgift

Which of the following is not normally an element of the Project Charter?
Select one alternative:

- The product description or a reference to this document
- The business need that the project was undertaken to address.
- Work package descriptions ✔
- The formal authorization to apply organizational resources to project activities ✖

Wrong. 0 of 1 marks.

10 Ny uppgift

You monitored figures on cost and planned/earned value for each individual project week until the data date at the end of the sixth week. The values at the end of the Six week were: AC= $100,000, EV= $120,000, PV= $110,000. What is the status of this project at this date?
Välj ett alternativ:

- The project is ahead of schedule and over budget
- The project is behind schedule and over budget
- The project is ahead of schedule and under budget. ✔
- The project is behind schedule and under budget

Correct. 1 of 1 marks.

11 Ny uppgift

The values at the end of the Six week were: AC= $335,000, EV= $300,000, PV= $347,000. What is the status of this project at this date?

Välj ett alternativ:

- The project is ahead of schedule and under budget.
- The project is behind schedule and over budget ✓
- The project is ahead of schedule and over budget.
- The project is behind schedule and under budget

Correct. 1 of 1 marks.

12 Ny uppgift

In a software company a large number of simultaneously performed projects utilize the same groups of human and other resources. What is the term commonly used for this situation?

Välj ett alternativ:

- Resource pooling ✓
- Program management
- Concurrent engineering
- Resource over-allocation

Correct. 1 of 1 marks.

13 Ny uppgift

A project is managed by a project coordinator. Which of the following statements is most likely to be true?

.

Välj ett alternativ:

- The performing organization is doing "management by projects".
- The performing organization is a strong matrix.
- The performing organization is projectized.
- The performing organization is a weak matrix. ✓

Correct. 1 of 1 marks.

14 New Question

Which of the three preventive measures deal with risk?

- All three are preventive measures ✓
- Creating contingency reserves in money and time
- Developing a plan to minimize probability
- Developing a plan to minimize potential impact

Correct. 1 of 1 marks.

15 New Question

The purpose of the Idea phase is to ...
Select one alternative:

- Analyse and document project ideas and queries so that they can be evaluated in competition with other desired projects and investments. ✓
- Document customer queries so that we can identify key market trends that will affect the business in the future
- Analyse and document business objectives so that we can determine strategic advantages in the business model.
- Brainstorm project ideas and queries so that we can create an exhaustive list of all strategic threats.

Correct. 1 of 1 marks.

16 Ny uppgift

Which of the following explains the pygmalion effect while leading projects
Select one alternative:

- Higher expectations influence higher performance ✓
- Those who expect more van get less. ✗
- Working under better conditions creates team building
- good reinforcement can lead to results

Wrong. 0 of 1 marks.

17 New Question

A project goal is different from impact goal because
Select one alternative:

- A project goals deals with sub-goals or milestones and deliverables while impact goal has a long term business value. ✓
- A project goal is a responsibility of project owner while impact goal is a responsibility of project team
- A project goal uses SWOT analysis while an impact goal uses SMART analysis
- An Impact goal deals with sub-goals or milestones and deliverables while project goal has a long term business value.

Correct. 1 of 1 marks.

18 New Question

All projects are limited by a deadline and a budget and quality, it is therefore important that project ´s priorities are clear. Who decides on what is the most important ?
Select one alternative:

- Steering committee
- Project Manager ✗
- Project Owner ✓
- Project group

Wrong. 0 of 1 marks.

19 New Question

Which of the following is not part of the DISC theory
Select one alternative:

- Compliance
- Influence
- Staffing ✓
- Dominance

Correct. 1 of 1 marks.

20 New Question

What is the 100% rule of the WBS?
Select one alternative:

- The sum of the activities in the bottom/lowest level of the A WBS should not compose 100% of the project
- A WBS should consist of all activities of the project, more than 100% to allow flexibility of the critical path
- None of the above
- A WBS should contain all the work included in the project ✓

Correct. 1 of 1 marks.

21 Ny uppgift

Which of the following describes an "**Activity plan**"
Välj ett alternativ:

- A logical network that shows the order goals which should be SMART
- A logical network shows the order in which the project activities will be handed over
- A logical network shows the order in which the project activities will be performed ✓
- A logical network shows the order in which the project activities will be financed

Correct. 1 of 1 marks.

22 New Question

Which of the following tools would be suitable to present the scope of the project
Select one alternative:

- Work Breakdown Structure ✓
- Organizational Breakdown Structure
- SWOT analysis
- Iron triangle

Correct. 1 of 1 marks.

23 New Question

You are the project manager for a seminar and training session that approximately 2,000-2500 employees will be attending. The employees attending the training will receive compensation for the travel expenses. You have rented a hall for the seminar and purchased sufficient meals and drinks for 2500 person; however, you are unsure exactly how many people will attend. Moreover, the number of tables required will change depending on attendance.

Which of the following describes the cost of the furniture and the cost of renting the hall ?
Select one alternative:

- Cost for furniture should be considered as variable cost and cost of renting the hall should be considered as direct cost
- Cost for furniture should be considered as fixed cost and cost of renting the hall should be considered as fixed cost
- Cost for furniture should be considered as variable cost and cost of renting the hall should be considered as indirect cost
- Cost for furniture should be considered as variable cost and cost of renting the hall should be considered as fixed cost

Correct. 1 of 1 marks.

24 New Question

1. We can calculate the probability of a project being on budget using
   $C_{estimated} = (C_{max} + 3C_{likely} + C_{min}) / 5$

   What is the $C_{estimated}$ for a project that has an estimated cost of €1200, if similar projects have cost as little as €1000 and occasionally as much as €2000?

Select one alternative:

- € 2 000,00
- € 1 000,00
- € 1 250,00
- € 1 320,00 ✓

Correct. 1 of 1 marks.

25 New Question

What does the term "Sprint Backlog" mean within the agile method ?

- Prioritized tasks to be executed within a stage with a defined length ✓
- Prioritized tasks to be executed within a shortest time
- Prioritized tasks to be executed within the critical path
- Prioritized tasks to be executed when initial plans are not changes

Correct. 1 of 1 marks.

26 New Question

In the Program Evaluation and Review Technique (PERT), what does Pessimistic (P) stand for ?
Select one alternative:


- The cost/duration of the activity, based on a realistic effort assessment for the required work and any predicted expenses.
- The activity cost/duration based on an analysis of the worst-case scenario for the activity
- The activity cost/duration based on an analysis of the best-case scenario for the activity.
- The activity cost/duration based on an analysis of the local -case scenario for the activity

Correct. 1 of 1 marks.

27 Ny uppgift

The Project Manager drew the network diagram that is demonstrated below. Given the duration, and assuming the project starts at zero days. Please fill the ES, EF, LS, LF, and SL,for each activity. What is the critical path and total duration of this Project ?

Activity	Duration
A	2
B	15
C	10
D	13
E	18
F	15
G	10
H	5

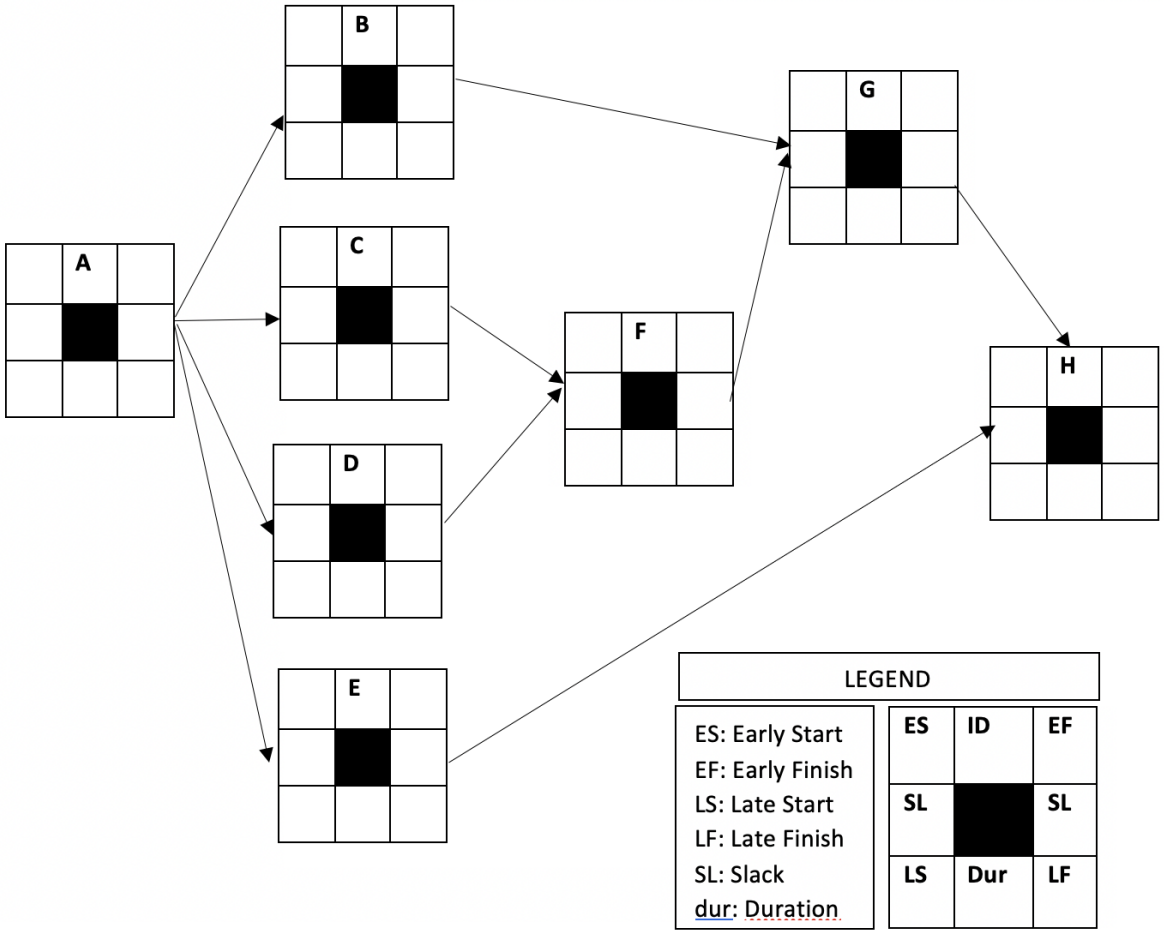

Select one alternative:

- The critical path is A,D,F,G,H and duration of project is 44 days.
- The critical path is A,D,G,H and duration of project is 45 days.
- The critical path is A,D,F,G,H and duration of project is 45 days. ✔
- The critical path is A,D,F,G,H and duration of project is 25 days.

Correct. 1 of 1 marks.

28 New Question

In making an investment in a project, investors require
Select one alternative:

- The direct benefits from the project to be more than the investment in the project ✔
- The direct benefits from the project to be less than the investment in the project
- The direct benefits from the project to be equal to the investment in the project
- The sum of the direct and indirect benefits from the project to be more than the investment in the project ✖

Wrong. 0 of 1 marks.
