CANDIDATE

1106C-0009-FJJ

TEST

1TS327 Industrial Project Management I

Subject code	--
Evaluation type	--
Test opening time	24.10.2022 08:00
End time	24.10.2022 09:30
Grade deadline	--
PDF created	01.10.2023 02:24

Copy%20of Examiner’s instructions

Examiner’s instructions

1. The exam includes 30 questions
2. All questions are complusory

1 The steering committee is responsible for…

The steering committee is (among other things) responsible for…
Select one alternative:

- Managing project activities
- Approving the project plan ✓
- Following up on the project goals
- Providing the project with resources

Correct. 1 of 1 marks.

2 Project life cycle Pre-study result

Which of the following statements is **not** true?
Select one alternative:

- If a project is rejected at the end of the Pre-study phase it can be modified and re-assessed in the future.
- If a project is accepted at the end of the Pre-study phase it advances to the Planning phase
- If a project is rejected at the end of the Pre-study phase it may still be interesting in the future if circumstances change
- If a project is rejected at the end of the Pre-study phase the Pre-study report and associated documents are classified documents and may not be viewed by individuals external the Pre-study group

Correct. 1 of 1 marks.

3 Accrual based accounting definition (alt 2)

Accrual based accounting:
Select one alternative:


- Connects cumulative costs to the customer
- Connects insurance costs to the complete time plan
- Connects individual monthly costs to the schedule
- Connects the project's cumulative costs to the schedule

Correct. 1 of 1 marks.

4 Planning tools network diagram (Alt 2)

The Project Manager drew the network diagram that is demonstrated below. What is the critical path and total duration of this project?

Activity	Duration
A	2
B	15
C	14
D	13
E	18
F	15
G	10
H	5

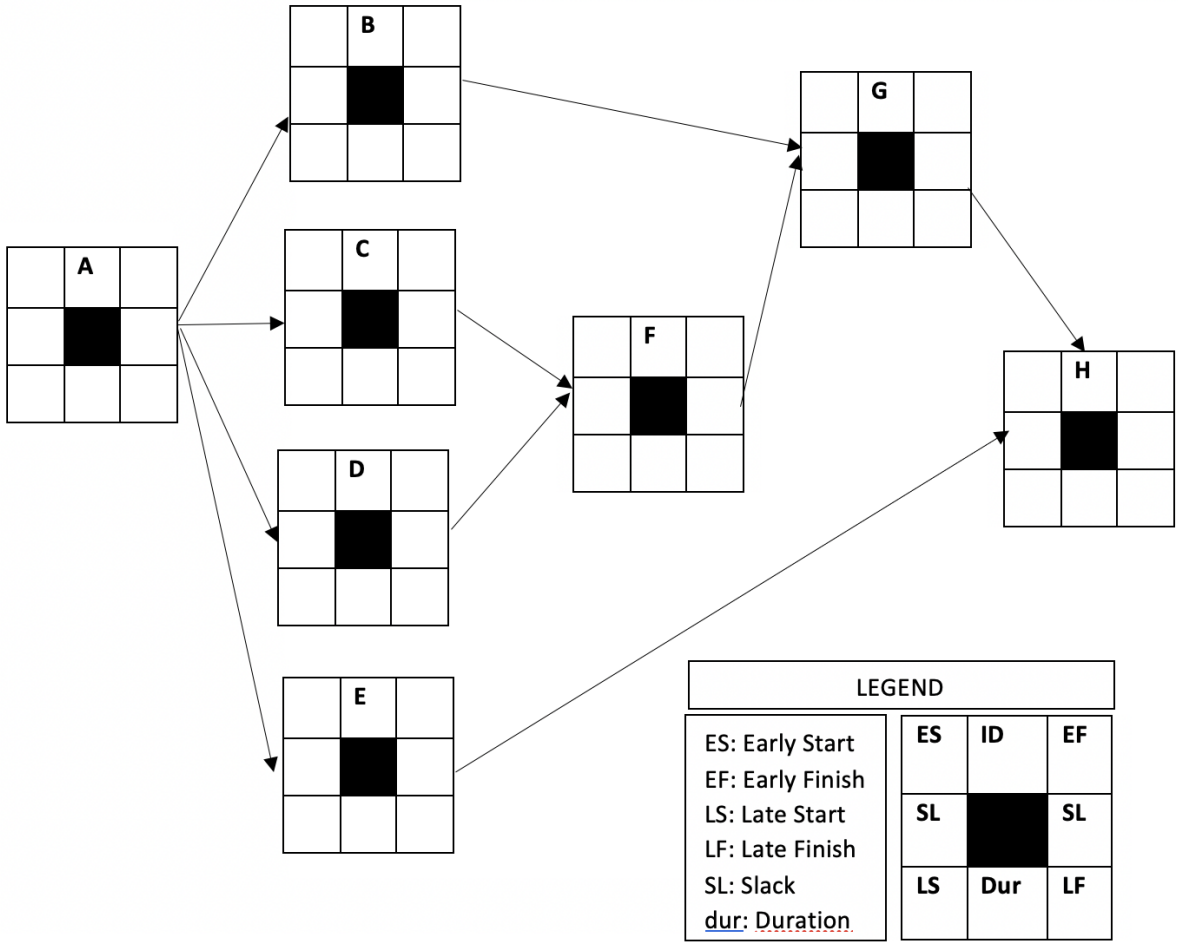

Select one alternative:

- The critical path is A,C,G,H and duration of project is 46 days.
- The critical path is A,C,F,G,H and duration of project is 25 days.
- The critical path is A,C,F,G,H and duration of project is 46 days. ✓
- The critical path is A,D,F,G,H and duration of project is 45 days.

This page is not part of the exam


Activity	Duration
A	2
B	15
C	10
D	13
E	18
F	15
G	10
H	5

Correct. 1 of 1 marks.

5 Find the critical path and duration

Air Control Company initiated a project consisting of eight activities. A, B, C, D, E, F, G and H. The duration for the activities is seen in the table below. The project manager drew the network diagram that can be seen below. Find the critical path and the total duration of the project.

Activity	Duration
A	2
B	15
C	10
D	13
E	18
F	15
G	10
H	5

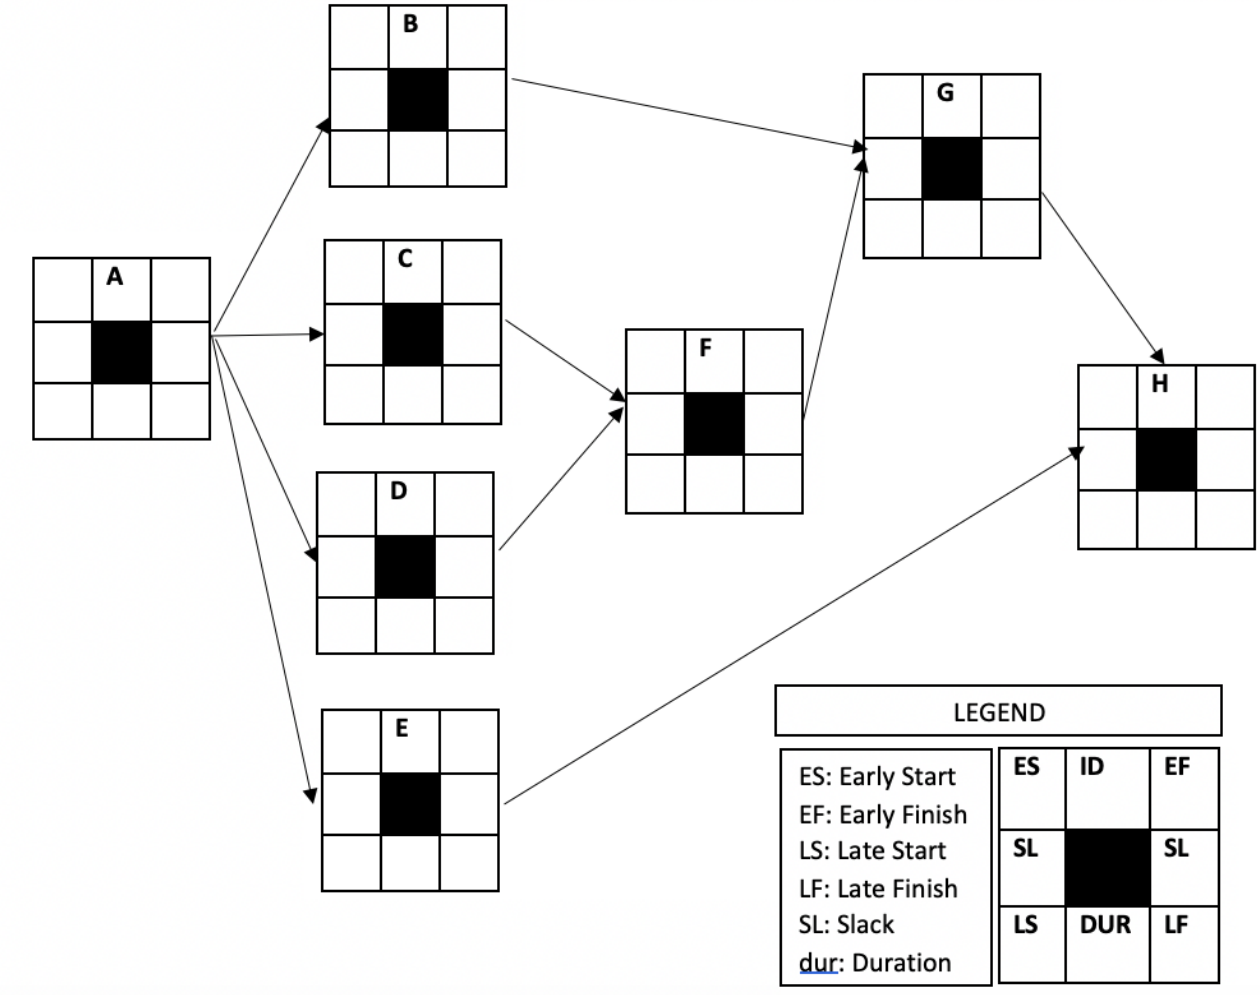


Select one alternative:

- The critical path is A,D,F,G,H and duration of project is 88 days
- The critical path is D,C,G and duration of project is 40 days
- The critical path is F,G,H and duration of project is 98 days
- The critical path is A,D,F,G,H and duration of project is 45 days ✓

Correct. 1 of 1 marks.

6 What type of planning method is this Gantt scheme an example of?

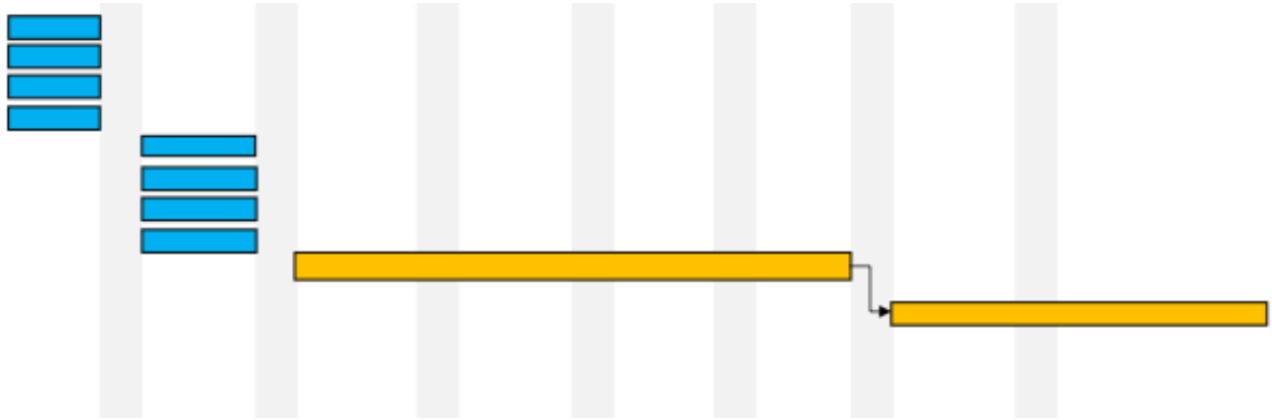

What type of project planning model is this Gantt scheme an example of?

Select one alternative:

- None of the alternatives ✗
- Stage-gate
- Concurrent engineering
- Agile planning ✓

Wrong. 0 of 1 marks.

7 A project goal is different from impact goal because

A project goal is different from impact goal because

Select one alternative:

- A project goal is a responsibility of project owner while impact goal is a responsibility of project team
- A project goals deals with sub-goals or milestones and deliverables while impact goal has a long term business value. ✔
- A project goal uses SWOT analysis while an impact goal uses SMART analysis
- An Impact goal deals with sub-goals or milestones and deliverables while project goal has a long term business value.

Correct. 1 of 1 marks.

8 Fixed and variable costs

Which of the following types of cost is directly attributable to the work of project such as team travel, recognition, team wages

Select one alternative:

- Fixed Costs
- Direct Costs ✔
- Indirect Costs ✖
- Variable Costs

Wrong. 0 of 1 marks.

9 Iron triangle definition

Which of the following variables is **NOT** part of the iron triangle?
Select one alternative:

- Time
- Cost
- Measurable ✓
- Quality

Correct. 1 of 1 marks.

10 Tools for scope

Which of the following tools would be suitable to present the scope of the project
Select one alternative:

- Iron triangle
- Work Breakdown Structure ✓
- Organizational Breakdown Structure
- SWOT analysis

Correct. 1 of 1 marks.

11 Predicting and controlling costs can be a problem for the Project manager because:

Select the alternative which normally is **NOT** a reason for why it is problematic for the project manager to predict and control costs within a project.

Select one alternative:

- The unique nature of projects is different to regular management control. ✗
- Many projects are primarily resource-limited (i.e. cost).
- Project costs are the largest component of organisations' operating costs ✓
- Many projects are sold with the price as a negotiation variable.

Wrong. 0 of 1 marks.

12 Alternative costs

Given the parameters below which alternative should be chosen according to the model for expected monetary value?

Select one alternative:

- 20% to earn 350 000, 80% to loose 100 000
- 40% to earn 40 000, 60% to loose 10 000 ✓
- 10% to earn 1 000 000, 90% to loose 200 000

Correct. 1 of 1 marks.

13 Investment calcs

A project manager performs Earned Value Analysis and finds the following results:

AC (actual cost) = 220 000
PV (planned value) = 250 000
EV (Earned value) = 220 000

What is the case for CV (cost variance)?
Select one alternative:

- CV = -30,000
- CV = 30,000
- CV = 1
- CV = 0 ✓

Correct. 1 of 1 marks.

14 Roles ref group

Which of the following roles suits the "Reference group" in a given project ?
Select one alternative:

- Form alternative opinions ✗
- Lead project changes
- Forum for testing ideas ✓
- Conduct new assesments

Wrong. 0 of 1 marks.

15 What is a critical path?

What is the critical path?
Select one alternative:

- Activities that do not impact completion time.
- Activities that determines the earliest possible finishing time for a project ✓
- Shows activities that should be monitored all the time until project closure
- Activities that determines the longest possible finishing time for a project

Correct. 1 of 1 marks.

16 When is an agile method the right choice

Which of the following are examples of when it is fitting to use agile project methodology?
Select one or more alternatives:

- ☐ The requirements are unclear ✓
- ☐ The goals are clear
- ☑ A result that can be used quickly is desired ✓
- ☐ There is a fixed deadline

Partially Correct. 1 of 2 marks.

17 Accrual based accounting definition

Accrual based accounting:
Select one alternative:

- Connects insurance costs to the project risks
- Connects individual monthly costs to the schedule
- Connects the project's cumulative costs to the schedule ✓
- Connects cumulative costs to the project manager

Correct. 1 of 1 marks.

18 Project status earned value, budget and schedule

You monitored figures on cost and planned/earned value for each individual project week until the data date at the end of the sixth week. The values at the end of the sixth week were:

AC (actual cost) = $200,000
EV (Earned value) = $220,000
PV (planned value) = $210,000.

What is the status of this project at this date?
Select one alternative:

- The project is behind schedule and over budget
- The project is ahead of schedule and under budget. ✓
- The project is ahead of schedule and over budget
- The project is behind schedule and under budget

Correct. 1 of 1 marks.

19 Project costs are under budget when CPI

Project costs are under budget when

Select one alternative:

- CPI > 1 ✓
- CPI < 1
- SPI = 1
- CPI = 0

Correct. 1 of 1 marks.

20 Project organisation roles: project coordinator and matrix org

A project is managed by a project coordinator. Which of the following statements is most likely to be true?

Select one alternative:

- The performing organization is projectized.
- The performing organization is doing "management by projects".
- The performing organization is a weak matrix. ✓
- The performing organization is a strong matrix.

Correct. 1 of 1 marks.

21 Belbin’s Team Roles is a model used for…

Belbin’s Team Roles is a model used for…
Select one alternative:

- Understanding project goals
- Team coordination
- Team composition ✓
- Understanding project activities

Correct. 1 of 1 marks.

22 What does the term "Sprint Backlog" mean within the agile method

What does the term "Sprint Backlog" mean within the agile method ?

- Prioritized tasks to be executed within the critical path
- Prioritized tasks to be executed when initial plans are not changes
- Prioritized tasks to be executed within a shortest time
- Prioritized tasks to be executed within a stage with a defined length ✓

Correct. 1 of 1 marks.

23 What is the 100% rule of the WBS?

What is the 100% rule of the WBS?
Select one alternative:

- A WBS should consist of all activities of the project, more than 100% to allow flexibility of the critical path
- None of the above
- The sum of the activities in the bottom/lowest level of the A WBS should not compose 100% of the project
- A WBS should contain all the work included in the project ✓

Correct. 1 of 1 marks.

24 A stakeholder analysis provides a comprehensive overview focusing exclusively on

A stakeholder analysis provides a comprehensive overview focusing exclusively on
Select one alternative:

- Individuals who will deliberately have a positive or negative affect on the result of the project execution or successful project completion
- Individuals and organizations who are actively involved in the project, or whose interests may be positively or negatively affected as a result of project execution or successful project completion. ✓
- Suppliers who could be actively involved in the project, or whose business offerings may positively or negatively affect the project outcome.
- Individuals and organizations who are do not want to be involved in the project, but whose interests may be positively or negatively affected as a result of project execution or successful project completion.

Correct. 1 of 1 marks.

25 Tollgates vs Milestones definition

Which of the following statements regarding milestones and tollgates is true?

Select one alternative

- A milestone is a checkpoint after the completion of an activity, often used to assess the health of a project, whereas a tollgate is a pre-determined point at which the project ✔ ner and steering committee decide if the project should continue.
- A milestone is a pre-determined point at which the project owner and steering committee decide if the project should continue, whereas a tollgate is a checkpoint after the completion of an activity, often used to assess the health of the project team.
- A milestone is an ad-hoc decision point at which the project owner and steering committee decide if the project should continue, whereas a tollgate is a checkpoint after the completion of an activity, often used to assess the health of a project.
- None of these statements are true. ✖

Wrong. 0 of 1 marks.

26 Estimating costs name

You have been tasked with estimating the costs for a project, but don't have the time or the deep technical expertise to estimate the costs in detail. To arrive at your estimate you search the company database to find similar projects that the company has completed. You also find the name of a project manager who worked on some of these past projects and ask to meet them to go through their estimate and the resulting costs.
This method of cost estimating is widely known as:
Select one alternative:

- PERT
- Bottom up
- Horizontal estimates
- Top down ✔

Correct. 1 of 1 marks.

27 Which of the following is not part of the DISC theory

Which of the following is not part of the DISC theory
Select one alternative:

- Influence
- Dominance
- Compliance
- Staffing ✓

Correct. 1 of 1 marks.

28 The four quadrants of the Positioning map are....

A project's strategic value can be compared with its expected economic value using a positioning map. The four quadrants of the Positioning map are....
Select one alternative:

- Mandatory, Value decreasing, Rationalising, and Empowering
- Consultatory, Value Increasing, Rationalising, and Independent
- Mandatory, Value Increasing, Rationalising, and Infrastructural ✓
- Mandatory, Strategy Increasing, Conventionalising, and Infrastructural

Correct. 1 of 1 marks.

29 Cultural differences

Which of the following statements is not true?
Välj ett alternativ:

- There is a common ground for people from different cultures on which they can interact without unsolvable conflicts ✗
- Cultural differences are a resource to be fully utilized.
- Cultural differences will always be an obstacle to be overcome. ✓
- Culture is a critical lever for competitive advantage.

Wrong. 0 of 1 marks.

30 Definition Iron Triangle

Which of the following is not part of the iron triangle
Select one alternative:

- Deliverables ✓
- Quality
- Cost
- Times

Correct. 1 of 1 marks.
