ℹ Information to students

Exam instructions

This exam is for the following courses:
1TS327; Industrial Project Management I
1KB726; Applied Energy Storage with Project Management

Dear student, welcome to Project Management Exam.

1. The exam consists of 30 questions. All questions are compulsory.

2. Each question is worth one point, leading to a total score of 30 points.

3. Permitted aids: You are allowed to bring a calculator during this exam, and an English translating dictionary in book form is allowed. All other notes or books are NOT allowed. This is an individual exam and closed book exam

4. The exam can be navigated at the bottom of the page, so if you are not sure about an answer, you may bookmark it and return to it later.

5. Remember to finish your exam and save it before you submit it.

6. To pass the exam, you will need at least 13 points

Formulas that might be useful
PERT: Expected time = (O + 4M + P) / 6
SPI = EV / PV.
CPI = EV/AC

Note; In the event that I am not present in the exam room, please do not hesitate to contact me at mob ; 0761 188 889. The invigilators will assist you in making the call if you require any clarification.

I wish you the best of luck

Grading
5: 26
4: 19
3: 13
U: 12 and below

1 Iron triangle definition

Which of the following variables is **NOT** part of the main dimensions of the iron triangle?
Select one alternative:

- ○ Risk ✔
- ○ Quality
- ○ Time
- ○ Cost

Maximum marks: 1

2 New Question

If the **scope** of a project increases but the **budget** and **time** remain unchanged, which of the following is likely to be affected?
Select one alternative:

- ○ Team motivation
- ○ Project quality ✔
- ○ Stakeholder engagement
- ○ Project communication

Maximum marks: 1

3 New Question

During the execution phase of a project, what is the **primary** responsibility of the project manager?
Select one alternative:

- Defining project objectives and deliverables.
- Performing a detailed risk analysis for all future phases of the project
- Developing the project budget and allocating resources.
- Monitoring and controlling project work to ensure alignment with the plan. ✔

Maximum marks: 1

4 New Question

Which of the following is not part of the DISC theory ?
Select one alternative:

- Compliance
- Influence
- Staffing ✔
- Dominance

Maximum marks: 1

5 New Question

Which of the following is a critical deliverable of the pre-study phase?
Select one alternative:

- Risk management plan
- Work Breakdown Structure (WBS)
- Project charter ✔
- Milestone chart

Maximum marks: 1

6 New Question

If a project's Schedule Performance Index (SPI) is 0.85 and the Cost Performance Index (CPI) is 1.1, what can be concluded?
Select one alternative:

- The project is behind schedule but under budget ✔
- The project is ahead of schedule and over budget
- The project is ahead of schedule and under budget
- The project is on time but under budget

Maximum marks: 1

7 New Question

In project management, what distinguishes a project goal from an impact goal?
Select one alternative:

- Project goals are broader and long-term, while impact goals are specific and immediate
- Project goals are concerned with larger societal impacts, while impact goals are limited to the project's scope.
- Project goals focus on transformative changes, while impact goals pertain to the completion of project tasks
- Project goals define the project's deliverables and outcomes, while impact goals represent broader and longer-term benefits. ✔

Maximum marks: 1

8 Ny uppgift

For a specific project task, the optimistic duration estimate is 5 days, the most likely estimate is 8 days, and the pessimistic estimate is 12 days. What is the expected duration for this task using PERT?
Select one alternative:

- 8.17 days ✔
- 12.33 days
- 10.00 day
- 6.67 days

Maximum marks: 1

9 Ny uppgift

In a solar energy project, the Planned Delivery (PD) for the solar farm was originally set at 12 months. However, due to project delays, the Schedule Performance Index (SPI) is currently at 0.80. What would be the is the forecasted delivery for the project?
Select one alternative:

- 6
- 12
- 17
- 15 ✔

Maximum marks: 1

10 Ny uppgift

In a construction project, the Planned Value (PV) is $50,000, and the Earned Value (EV) is $40,000. What is the Scheduling Performance Index (SPI), and is the project behind schedule or not?
Select one alternative:

- SPI = 1.25; Yes, the project is behind schedule.
- SPI = 1.25; No, the project is ahead of schedule.
- SPI = 0.8; Yes, the project is behind schedule. ✔
- SPI = 0.8; No, the project is on schedule.

Maximum marks: 1

11 The project owner is responsible for:

The project owner is (among other things) responsible for:
Select one or more alternatives:

- [ ] The project's impact goals ✔
- [ ] Both the project's project goals and the project's impact goals
- [ ] The project's project goals
- [ ] Delegating and following up on activities

Maximum marks: 1

12 New Question

Given the following task durations, Task A = 4 days, Task B = 2 days, Task C = 6 days, Task D = 3 days. Task A and Task B can start simultaneously, but Task D depends on Task A. What is the critical path duration?
Select one alternative:

- ○ 13 days
- ○ 9 days
- ○ 7 days ✔
- ○ 12 days

Maximum marks: 1

13 Project life cycle Pre-study result

Which of the following statements is **not** true?
Select one alternative:

- ○ If a project is rejected at the end of the Pre-study phase it may still be interesting in the future if circumstances change
- ○ If a project is rejected at the end of the Pre-study phase it can be modified and re-assessed in the future.
- ○ If a project is accepted at the end of the Pre-study phase it advances to the Planning phase
- ○ If a project is rejected at the end of the Pre-study phase the Pre-study report and associated documents are classified documents and may not be viewed by individuals external to the Pre-study group ✓

Maximum marks: 1

14 Tools for scope

Which of the following tools would be suitable to present the scope of the project
Select one alternative:


- ○ Organizational Breakdown Structure
- ○ SWOT analysis
- ○ Work Breakdown Structure ✔
- ○ Iron triangle

Maximum marks: 1

15 Planning tools network diagram

A project manager has drawn the network diagram shown below. What is the critical path and the total time for the project?
The Project Manager drew the network diagram that is demonstrated below. Given the duration, and assuming the project starts at zero days. Find the total duration for the critical path ?

Activity	Duration
A	2
B	15
C	10
D	13
E	18
F	15
G	10
H	5

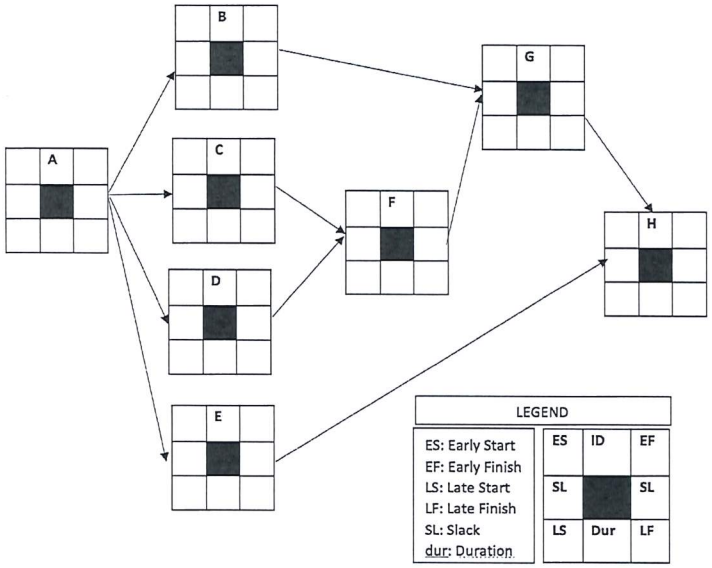

Select one alternative:

- The critical path is A,D,G,H and duration of project is 45 days.
- The critical path is A,D,F,G,H and duration of project is 45 days.
- The critical path is A,E,F,G,H and duration of project is 50 days. ✔
- The critical path is A,D,F,G,H and duration of project is 44 days.

Maximum marks: 1

16 The steering committee is responsible for...

The steering committee is (among other things) responsible for...
Select one alternative:

- Following up on the project goals
- Providing the project with resources
- Managing project activities
- Approving the project plan ✔

Maximum marks: 1

17 What is the 100% rule of the WBS?

What is the 100% rule of the WBS?
Select one alternative:

- A WBS should contain all the work included in the project ✔
- None of the above
- The sum of the activities in the bottom/lowest level of the A WBS should not compose 100% of the project
- A WBS should consist of all activities of the project, more than 100% to allow flexibility of the critical path

Maximum marks: 1

18 Project status earned value, budget and schedule

You monitored figures on cost and planned/earned value for each individual project week until the data date at the end of the sixth week. The values at the end of the sixth week were:

AC (actual cost) = $200,000
EV (Earned value) = $220,000
PV (planned value) = $210,000.

What is the status of this project at this date?
Select one alternative:

- The project is ahead of schedule and under budget. ✔
- The project is behind schedule and under budget
- The project is behind schedule and over budget
- The project is ahead of schedule and over budget

Maximum marks: 1

19 New Question

Which leadership style is best suited for dealing with a team that is struggling with motivation and deadlines?
Select one alternative:

- Transactional
- Servant leadership
- Transformational ✔
- Autocratic

Maximum marks: 1

20 New Question

Which of the following statements accurately differentiates a strong matrix from a weak matrix in project management?
Select one alternative:

- In a strong matrix, the project manager has less authority, while in a weak matrix, the functional manager has more authority.
- In a strong matrix, the functional manager has more authority, while in a weak matrix, the project manager has full control.
- In both strong and weak matrix organizations, the project manager and functional manager share equal authority.
- In a strong matrix, the project manager has more authority and control over resourc ✔, while in a weak matrix, the functional manager retains most of the control.

Maximum marks: 1

21 New Question

What is the impact of high-risk uncertainty in project planning?
Select one alternative:

- It requires increased budget allocation.
- It decreases project duration
- It requires more frequent risk assessments ✔
- It leads to early project closure

Maximum marks: 1

22 New Question

What is the primary responsibility of the Product Owner in a Scrum Team?
Select one alternative:

- Managing the development team
- Ordering and maintaining the Product Backlog ✔
- Ensuring that Scrum events take place
- Writing user stories for the team

Maximum marks: 1

23 New Question

Which of the following would reduce the Earned Value (EV) of a project?
Select one alternative:

- Increased actual cost (AC)
- Completing work ahead of schedule
- Delays in task completion ✔
- Spending less than planned

Maximum marks: 1

24 New Question

A project is a work form with a specif goal, which of the following is the logical flow according to the stage gate model?
Select one alternative:

- Initiating, Planning, Executing, Closing ✔
- Initiating, Planning, Executing
- Initiating, Executing, Planning, Closing
- Initiating & Executing

Maximum marks: 1

25 New Question

Which of the following statements best describes the purpose of the Sprint Retrospective?
Select one alternative:

- To plan the work for the next Sprint
- To inspect how the last Sprint went and identify improvements ✔
- To present the results of the Sprint to stakeholders
- To review the progress towards the Product Goal

Maximum marks: 1

26 New Question

What is the main and primary objective of project governance in an organization?
Select one alternative:

- To optimize the use of resources ✔
- To supervise marketing efforts
- To manage individual tasks within the project
- To handle customer feedback

Maximum marks: 1

27 What type of planning method is this Gantt scheme an example of?

Which of the following features is most characteristic of an Agile Gantt chart ?
Select one alternative:

- A strict sequence of tasks that cannot overlap, moving from one phase to the next.
- A single, linear timeline with distinct phases and clear "gates" between them.
- Overlapping tasks organized in iterative sprints with regular feedback loops. ✔
- A fixed plan with minimal adjustments once the project begins.

Maximum marks: 1

28 New Question

In the context of project risk management, what is the first step in the risk management process?
Select one alternative:

- Risk monitoring
- Risk identification ✔
- Risk response planning
- Risk analysis

Maximum marks: 1

29 New Question

What does the "critical path" in a project schedule represent?
Select one alternative:

- The tasks that have the least amount of float
- Activities on the critical path have zero slack (or float), meaning there is no flexibility in their start or finish times without delaying the project ✔
- The tasks that must be completed last
- The tasks that are easiest to complete

Maximum marks: 1

30 New Question

Using the data below, calculate the project's Earned Value (EV) at month 3: Planned Value (PV) = $15,000, Actual Cost (AC) = $14,000, and the work completed is 60%.
Select one alternative:

- $15,000
- $9,000 ✔
- $14,000
- $10,000

Maximum marks: 1
